

- 1 August 16, 2025**
Incident
Accident involving Streetcar 105 occurred. Repair program initiated.



- 2 Sep. – Nov. 2025**
Sun link assessment & initial repairs
Collision assessment; removal of damaged components; brake and propulsion testing; APS repairs; and removal of the damaged B-Cab windshield. Assessment, removal, repair, and testing activities performed.




- 3 Nov. – Dec. 2025**
ADOT inspection of 105



- 4 Dec. 2025–Apr. 2026**
Approval & process coordination




- 5 April–May 2026**
Inspection & reassembly
Articulation inspection and progressive reassembly of the interior, mirrors, handrails, paneling, and body structure. Reassembly advanced.

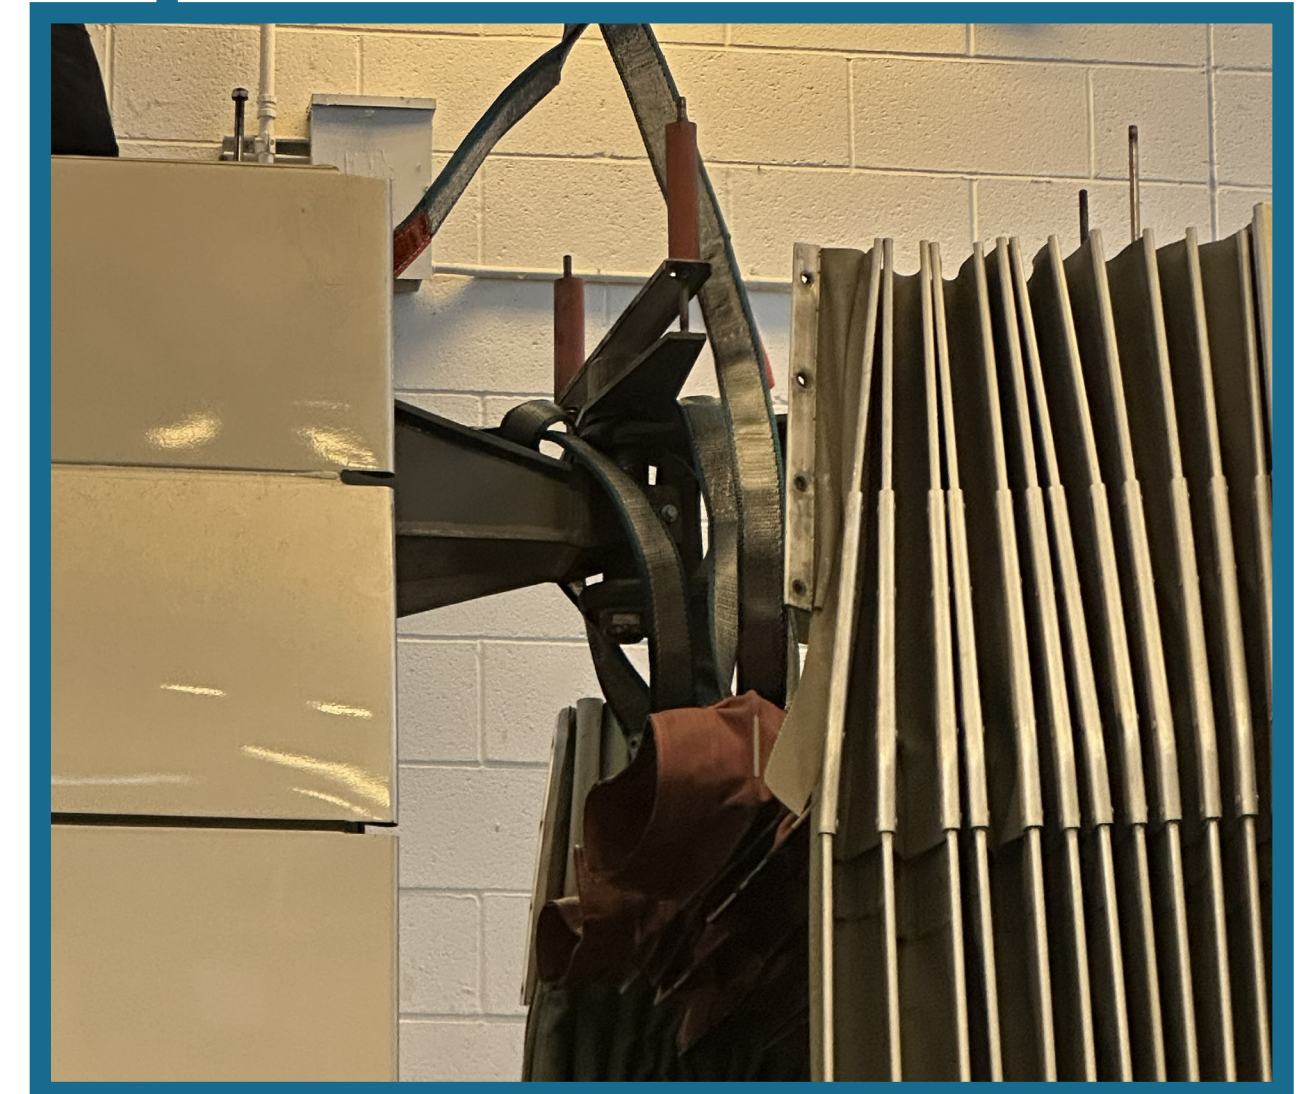


- 6 June 2026**
Body & systems work
Completion of much of the B-Cab body, glazing, bumper, window, mirror, and hydraulic-line work. Major collision-related body work substantially advanced.



- 7 July 2026**
Hunting-condition investigation
Truck replacement, ride-height adjustment, suspension alignment, spring and shim inspection, damper replacement, and repeated operational testing to investigate the B-Cab hunting condition. 10,000-mile inspection performed per ADOT request. Investigation and corrective testing continued.

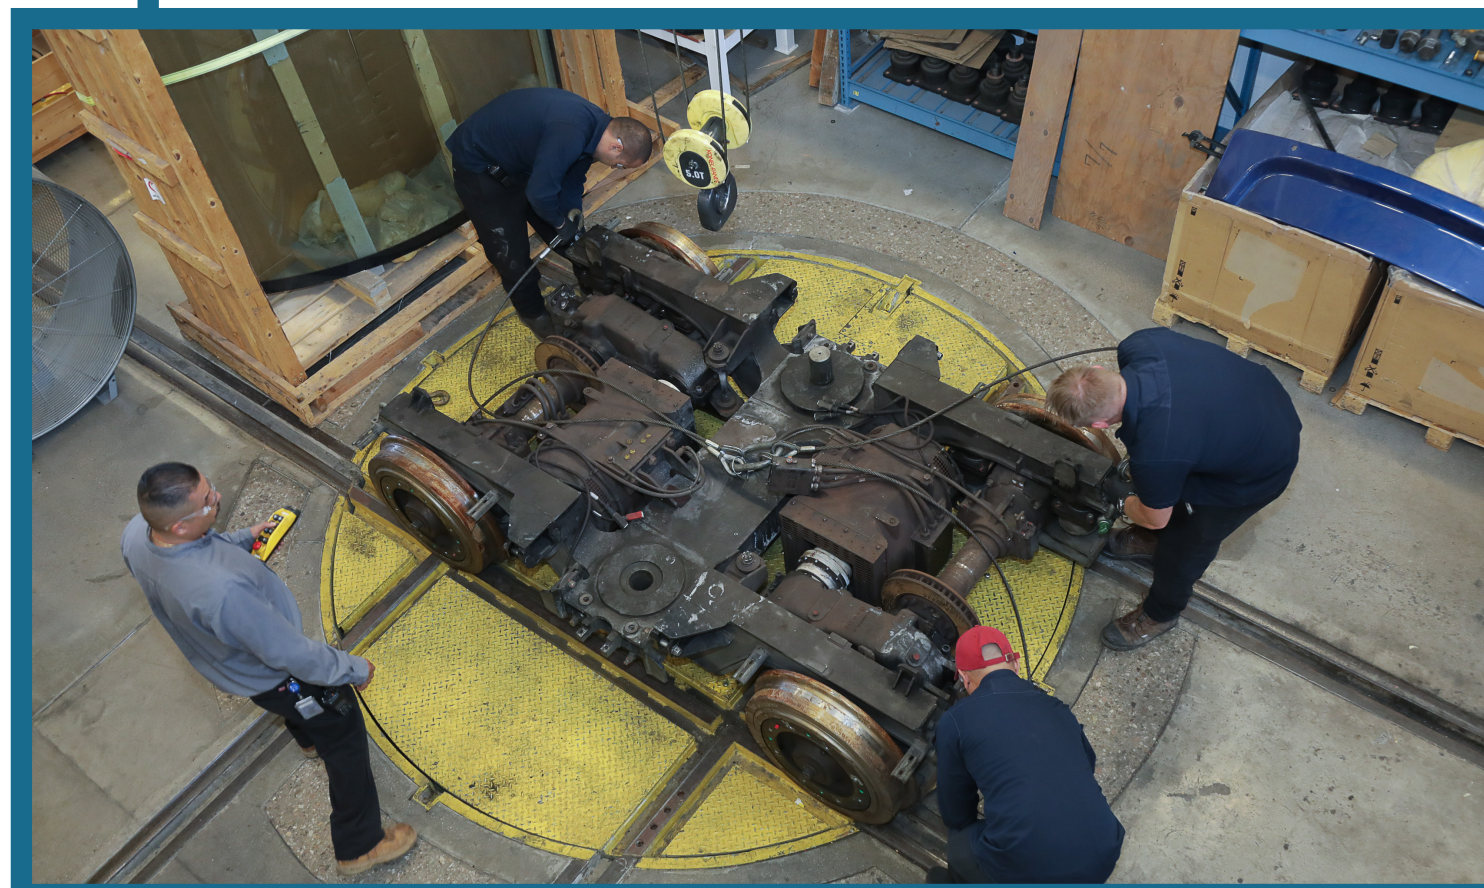

- 8 August 2026**
Testing and safety checks
All repairs and adjustments have been completed. The burn-in run prescribed by ADOT has also been successfully completed, and the streetcar is ready for service with no faults or issues noted. Ready for service.

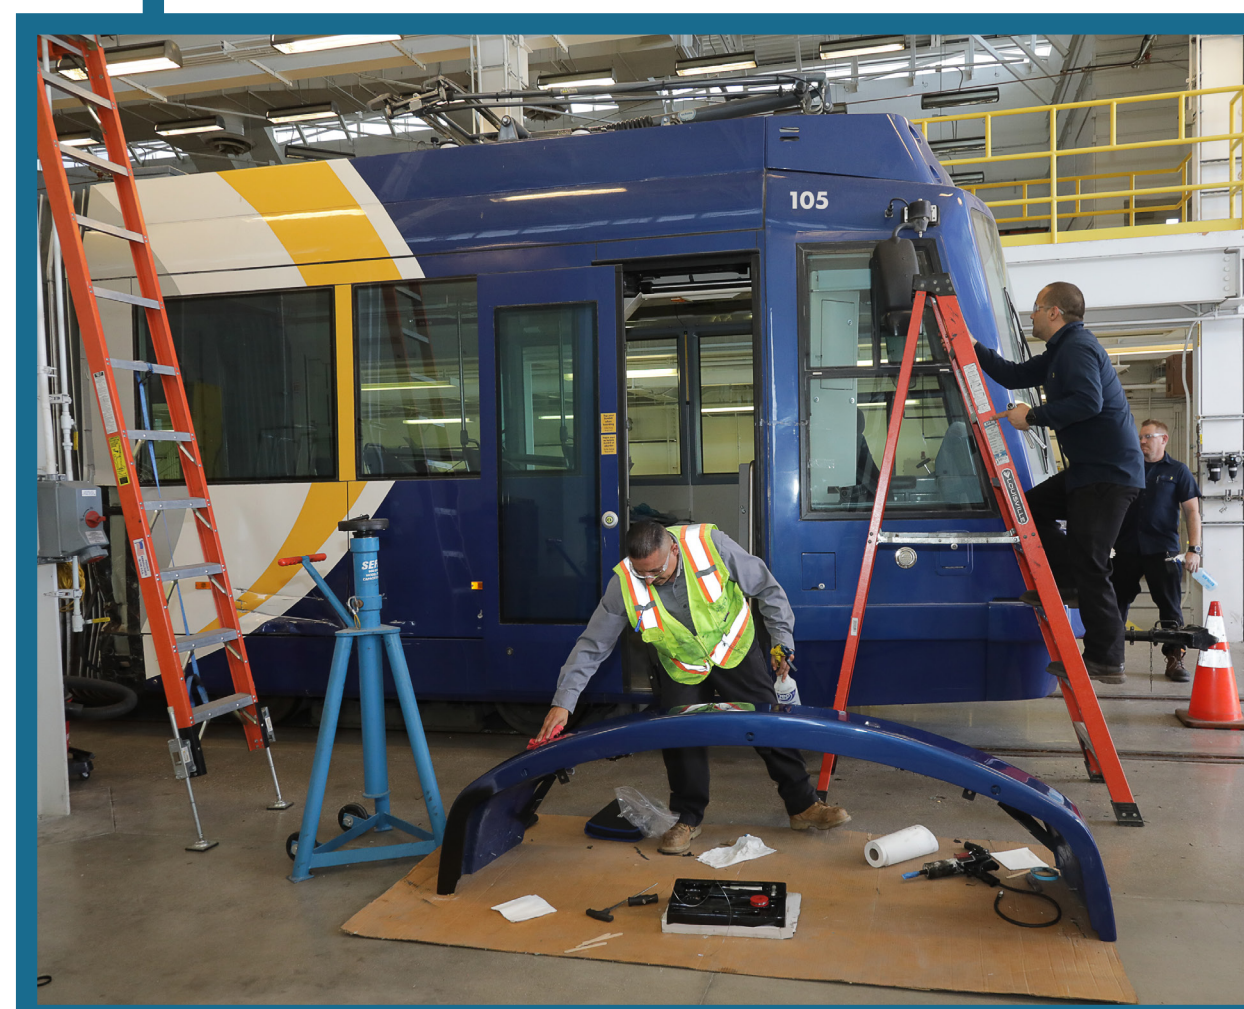

- 9 August 2026**
Sun Link Streetcar 105 returns to the track today!



Special thanks to the Sun Link Maintenance, Operations and Von's Carstar teams!
